

## AAPS Capital Improvements Program

# Huron High School Update 8-26-24

The AAPS Capital Improvements Program continues to develop and implement projects outlined in the 2019 Bond Campaign and the BOE approved Bond Plan. These improvements are consistent with the needs outlined in the facility condition assessment report.

### Project Information

Scope of Work	Location of Work
<p><b><u>Monorail Installation at Pool</u></b> Install a new 5 ton monorail hoist system for loading and unloading equipment, materials, and supplies to support the pool and filtration and future pool improvements.</p>	Huron Pool & Pool Mechanical Rooms
<p><b><u>Huron Pool Filtration Equipment Modernization</u></b> New pool pumps and tanks, new ADA lift for pool, new starter blocks, new electrical upgrade with new electrical switchgear and transformer for pool equipment, new filter pump pits and modification of existing surge pit in pool mechanical room. This work does not include any painting, pool tile or deck work, HVAC system revisions/changes, spectator area work, pool offices or locker rooms.</p>	Huron Pool & Pool Mechanical Rooms
<p><b><u>Huron Exterior Brick Wall, Roof Repair, Metal Siding Repair</u></b> Exterior Brick has been removed. There was a delay from the brick manufacturer and work began 8/19. Once work begins it will take approximately 4wks to complete. Work is anticipated to be complete towards the end of September, weather permitting. Repair roofing at several locations. Repair damaged metal siding at select exterior locations. This work does not include any painting, windows, doors, or planter boxes, paving, or sidewalks.</p>	Huron Building Exterior

### Project Contacts


Construction Manager Site Superintendent	Construction Manager Project Manager	AAPS Representative
Steven Witt	Timmie Snook	Chris Duru
Brix Corporation	Brix Corporation	Gilbane Building Company
734-608-1530	313-500-3447	312-661-2306
<a href="mailto:switt@brixcorporation.com">switt@brixcorporation.com</a>	<a href="mailto:tsnook@brixcorporation.com">tsnook@brixcorporation.com</a>	<a href="mailto:cduru@gilbaneco.com">cduru@gilbaneco.com</a>

### Project Schedule


TIMELINE:	Construction Activities
April 29, 2024	The pool is Closed for All Activities; Pool will be drained during the summer break for pool filter improvements.
June 14- September 13, 2024	Exterior Brick install. Brick was delayed from manufactured which extended the end date into September.
August 26, 2024	First Day of School for Students
September 27, 2024	Pool Reopen for Activities (Anticipated)

# AAPS Capital Improvements Program

Project Location & Maps:

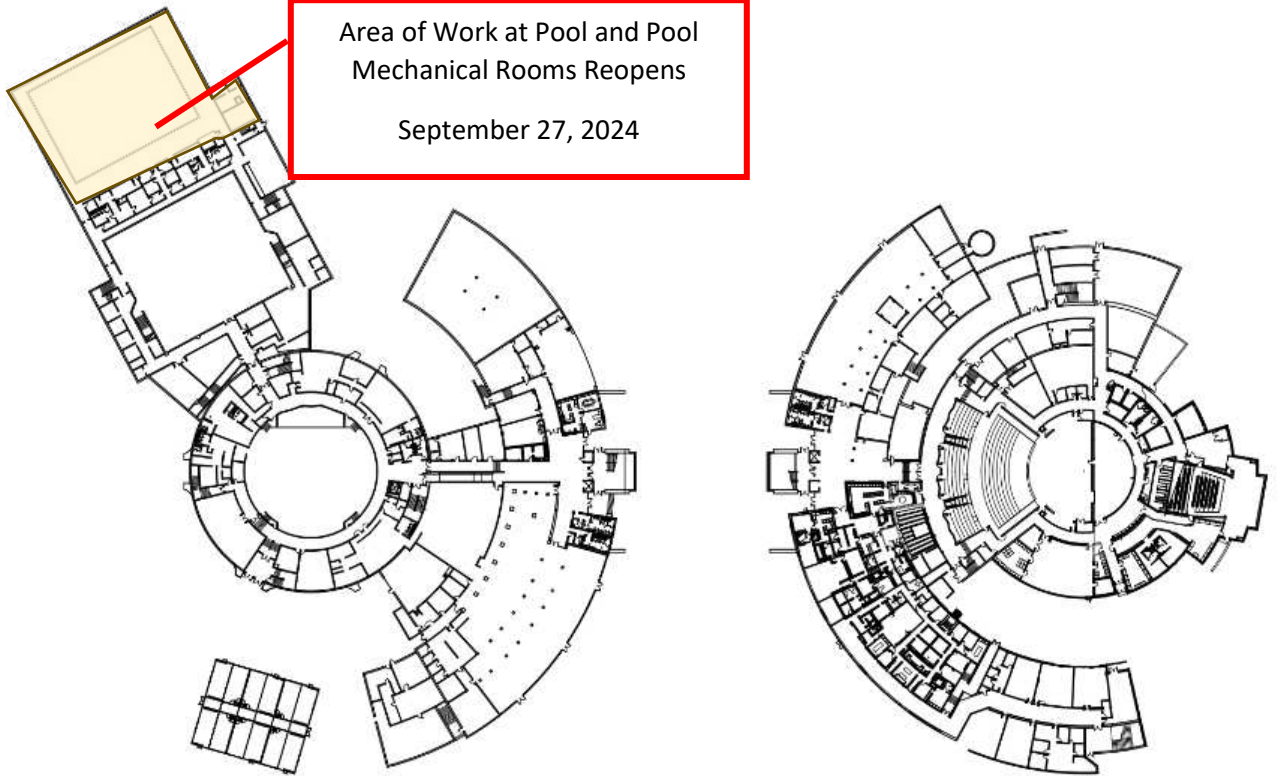

## AAPS Capital Improvements Program

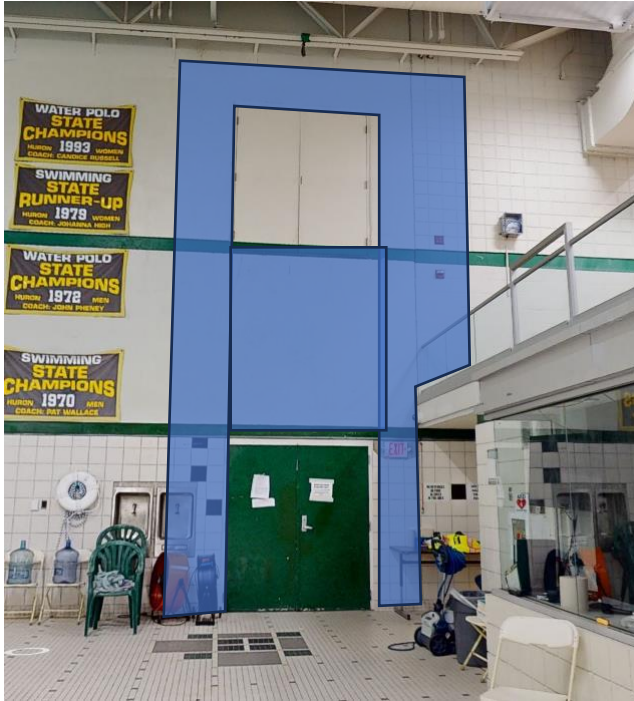

There may be areas that require coordination of the work to be completed, impacted staff/departments will be contacted directly.



[www.a2schoolsbond.org/staff-info](http://www.a2schoolsbond.org/staff-info)  
[www.a2schoolsbond.org](http://www.a2schoolsbond.org)
